BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-03-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of	Cum	20.32	0	0	03-09-22	01-02-23	151
2	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, key trenches, foundation of bridges and such simillar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting,	Cum	3973.78	2807.74	71	05-09-22	25-09-22	20
3	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150	Cum	665.72	446.57	67	20-09-22	05-10-22	15
4	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/basalt crushed graded coarse aggregates	Cum	4.04	0	0	05-09-22	25-02-23	173
5	Supplying, Fitting and Placing un-coated TMT bar Reinforcement in sub-structure complete as per Drawing and Technical Specifications.	Tonne	72.1	46.77	65	25-09-22	15-10-22	20
6	Providing and laying flamed finish Granite stone flooring in required design and patterns, in linear as well as curvilinear portions of the building all complete as per the architectural drawings with 18 mm thick stone slab over 20 mm (average) thick	Sqm	32	0	0	05-09-22	25-02-23	173

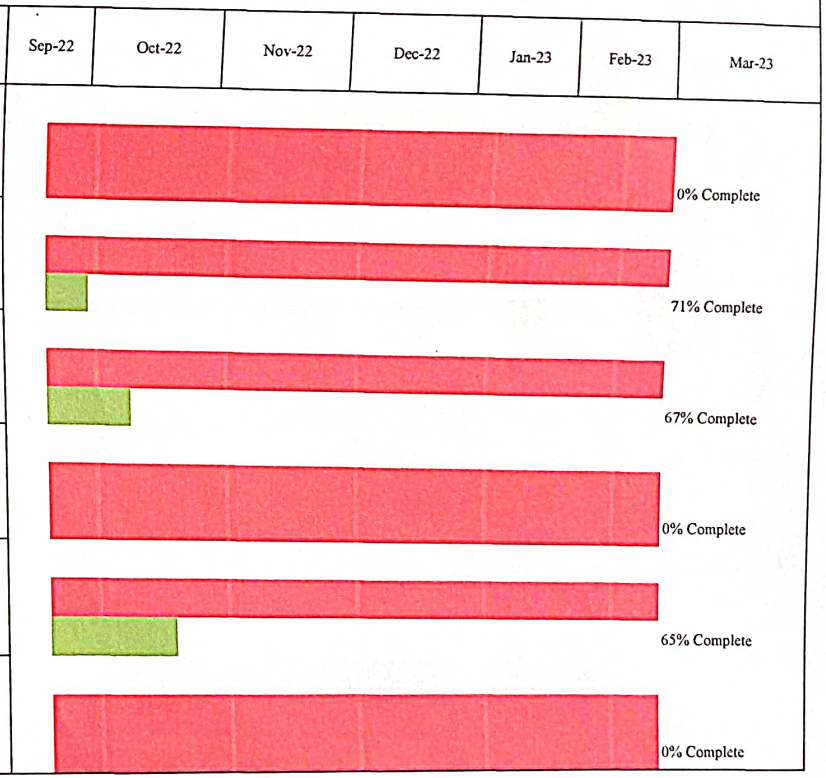

BRUHAT BENGALURU MAHANAGARA PALIKE

	:	Executive Engineer Yelahanka Division
ne me	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
	:	Rudraprasad Consultants
ıts	:	Karthik Rechan
lanager /Team Leader	:	03-09-22
Start Date	:	03-03-23
End Date	:	6 Months
Length in Months		

ssignment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
Providing and fixing G.I. chain link fabric fencing of required width in mesh size 25x25 mm made of G.I. wire of dia 3 mm including strengthening with 2 mm dia wire or nuts, bolts and washers as required complete as per the direction of Engineer-in-	Sqm	291.5	0	0	05-09-22	25-02-23	173
Fabricating, providing and erecting in position Hot dip galvanised Gate. Using 72*72*4.8mm Sq. GI Pipe frame with top pipe bending in heavy duty hydraolic press with sand packing and hot bending to form double arch as per drawing profile,20mm hot dip	Sqm	11.97	0	0	05-09-22	25-02-23	173
Demolishing cement concrete manually/ by mechanical means including disposal of material to the appropriate disposal area as per direction of Engineer-in-charge.	Cum	165.83	0	0	05-09-22	25-02-23	173
Removing and resetting of kerb stones	Mtr	840	1050	100	30-09-22	15-10-22	15
Removing and Resetting of Footpath Slab	Sqm	3980.71	44.2	1	30-09-22	15-10-22	15
Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The granite/trap/basalt crushed graded coarse	Cum	1034.98	756.85	100	10-10-22	30-10-22	20

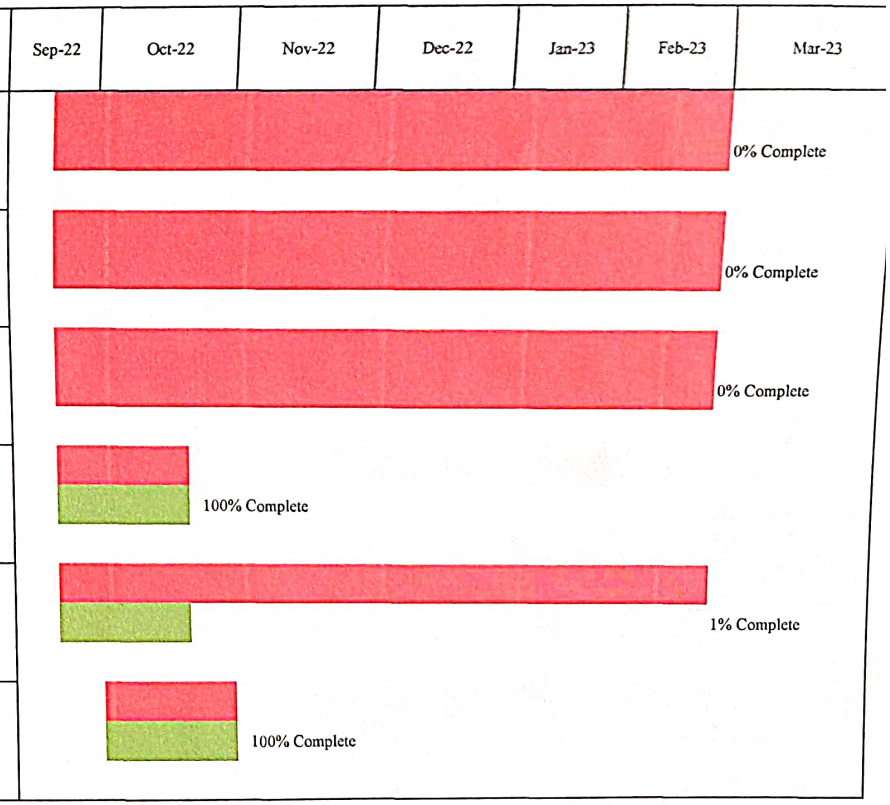

BRUHAT BENGALURU MAHANAGARA PALIKE

ame	:	Executive Engineer Yelahanka Division
ame	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
ts	:	Rudraprasad Consultants
anager /Team Leader	:	Karthik Rechan
rt Date	:	03-09-22
d Date	:	03-03-23
ngth in Months	:	6 Months

ment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
ply and fixing of Retro Reflective Single Arrow Road Name nboard of size 1600mm x 900mm made out of retro reflective eting conforming to Type XI standards of ASTM D 4956-09 & er IRC 67-2012 for full back ground of blue colour & white	Nos	87	0	0	05-09-22	25-02-23	173
pplying and Fixing of Molded Shank Raised Pavement Markers at's Eye made of polycarbonate and ABS moulded body and flective panels with micro prismatic lens capable of providing al internal reflection of the light entering the lens face and shall	Nos	80	0	0	05-09-22	25-02-23	173
ad for Disposal of Debris	Cum	7449.66	5892.75	92	05-09-22	15-12-22	101

= Planned %

= Executed %

RUDRAPRASAD CONSULTANTS BANGALORE

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಬ.ಬ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106
